


Main Street Improvement Project Update Aug. 4, 2020

Proposition 3 - Main Street Improvements

- Phase I (southern half of Main Street) is complete!
 - The efforts of Cox Commercial Construction over the past several weeks resulted in the completion of Phase I (the southern half of Main Street from Railroad to the divide on the east end.)
 - The major activities completed include:
 - Milling and partial excavation of the full length
 - New curb and gutters
 - Drainage improvements
 - New water and wastewater lines
 - New sidewalks and pedestrian lighting
- Phase II (northern half of Main Street) begins this Thursday, Aug. 6, 2020 and will last approximately 110 days.
 - The traffic pattern will shift to two-way traffic on the south side this Wednesday, Aug. 5 and will include road surface painting and marking for traffic control
 - Traffic signal lights will change to align to the traffic lanes
 - Erosion control measures will be completed by this weekend
 - Milling of the northern half will begin on Monday, Aug. 10
 - Excavation for the new 24" effluent force main will begin on Tuesday, Aug. 11
- Phase III of the project (full-width 2" surface overlay from Ash Street to the O'Reilly's Auto Parts driveway) is expected to begin shortly after the Thanksgiving holiday.

PROPOSITION 3 Main Street Improvements

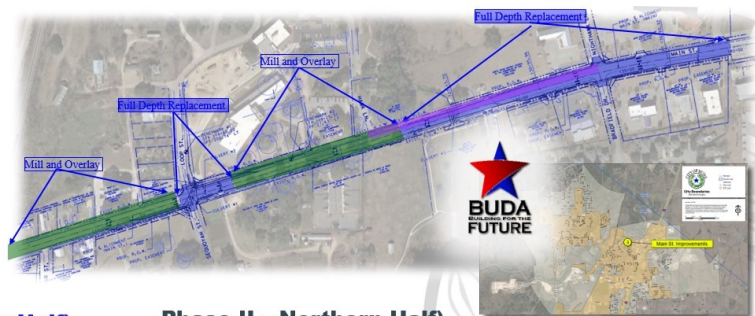


Phase I – Complete (Southern Half)

(381 Days: July 22, 2019 – August 6, 2020)

- ✓ Full length milling
- ✓ Full Depth excavation (in blue)
- ✓ Curb & Gutters
- ✓ Drainage
- ✓ Utility installation (sewer & water)
- ✓ Asphalt Base
- ✓ Sidewalks
- ✓ Pedestrian Lighting

Phase II – Northern Half

(T~110 Days: August 6 – ~Thanksgiving)



- ✓ Erosion Control
- ✓ 2-way traffic control shifts to southern side
- ✓ Painting and marking of roadway
- ✓ Milling of northern side
- ✓ Excavation for 24" Effluent Force Main
